# **Council House Building update**

- Phase 1 completed and occupied
- Phase 2 contracts awarded –start on site dates being confirmed
- Phase 2b contracts awarded start on site dates being agreed
- Phase 3, business case completed, mobilising the delivery team
- Phase 4 identifying sites




#### Phase 2

- Saffron Velodrome site 38 units. Contract award imminent, start on site October 21
- Lanesborough Road 37 units, very difficult site, in excess of 100 objections, planning application to be submitted in August and approval expected October. Contact awarded, expected start on site Jan 22



#### Velodrome site

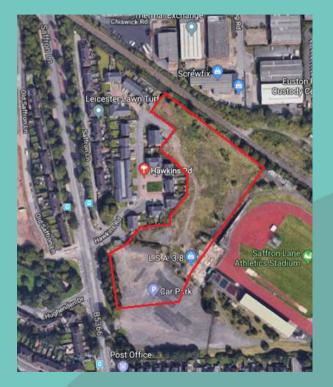







#### Milestone

Date	(Dates	indicate	comple	tion of	task)
------	--------	----------	--------	---------	-------

Tender Evaluation	20/07/21	
Tender Report	13/08/21	
Tender Award	30/08/21	
Preconstruction and RIBA 4 Design	16/11/21	
Start on Site	22/11/21	
Practical Completion	02/06/23	

Saffron Lane Dwelling Mix					
Dwelling Type	Number of Units				
1 Bed/2Person House	6				
2 Bed/4 Person House	8				
3 Bed/5 Person House	10				
4 Bed/8 Person House	4				
1 Bed/2 Person Bungalow	4				
2 Bed/4 Person Bungalow	3				
3 Bed/5 Person Bungalow	3				
Total	38				




# Lanesborough Road







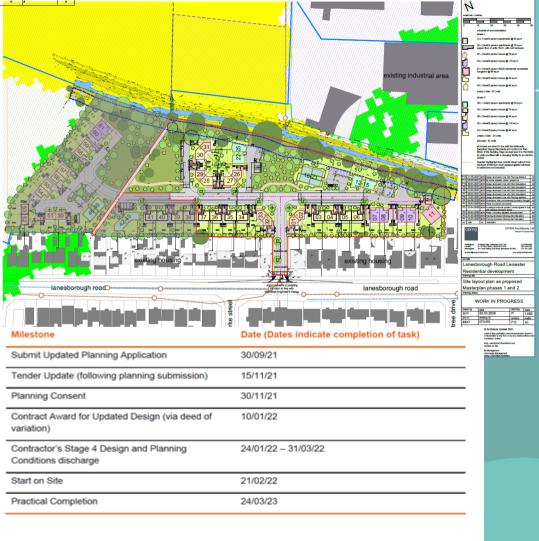

Lanesborough Road Dwelling Mix				
Dwelling Type	Number of Units			
1 Bed/2 Person Flats	12			
2 Bed/4 Person Flats	2			
2 Bed/4 Person House	7			
3 Bed/5 Person House	11			
4 Bed/8 Person House	4			
3 Bed/5 Person Bungalow	1			
Total	37			



#### Phase 2b sites

- Hydra Walk 2 units.
- Rockingham Close 3 units
- Austin Rise 8 units
- Whitteney Drive 5 units



#### **Rockingham Close**

Planning permission granted.3unitsContracted awardedStart on site date: October 21Completion date: June 22





#### **Whitteney Drive**

Planning permission expected october 5 units Contract award: October 21 (est) Start on site: January 22 Completion: December 22



#### **Austin Rise**

Planning permission granted 8 units Contract to be awarded – October 21 Start on site – April 22 Completion – March 23





#### Hydra Walk


Planning permission granted

2 units – conversion of former housing office

Contract awarded

Start on site : October 21

Completion Feb 22

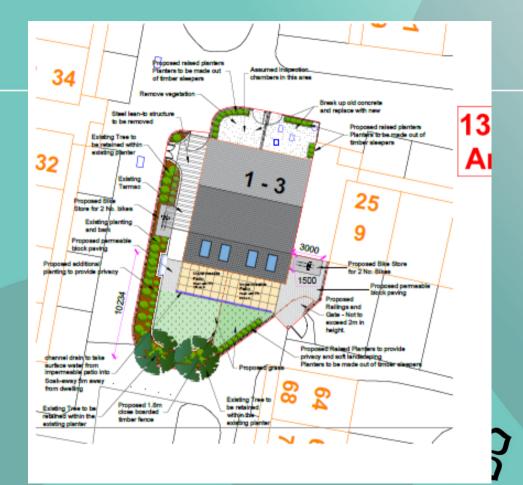

Leicester City Council

#### Phase 3 sites

#### **Site locations**

- 53 units of accommodation
- 7 sites across the city
- Smallest site has 2 units up to 18 units for largest site
- Ward councillors aware of sites
- Agreeing broader comms to local residents

#### **Milestone dates**

- Preplanning app- Dec 21
- Full planning –July22
- Tenders Jan 23
- Contract award March 23
- Start on site April 23
- Completion date Sept.



### **Climate emergency**

- Phase 1 was delivered to an enhanced building control standards
- Phase 2 and 2b, will be delivered to a standard that is 79% better that building control standard
- Phase 3, the environmental standard are currently being looked at with a view to achieving carbon zero.



### Summary

scheme	Number of units
Phase 1	29
Phase 2	75
Phase 2b	18
Phase 3	53
total	175



### Extra Care Scheme- update

- The two extra care schemes proposed for the city are currently on hold. (Tilling and Hamelin)
- This is an ASC lead piece of work in partnership with Housing
- These would have delivered 155 units towards the manifesto commitment to deliver 1500 new affordable homes by March 2023.
- We are currently looking at alternative procurement options to deliver both schemes
- We have started a soft market testing exercise to deliver a supported living scheme at The Exchange site, Eyres Monsell



### **General Acquisitions**

- Former council houses
- Majority are 2 & 3 bedrooms
- Trying to buy larger family homes
- Targeting leasehold former council homes
- Buying for NHS transforming care cases
- Trying to buy adapted homes



# What have we bought so far

- Number of properties brought in 2018/19: 33
- •
- 1 x 1 bed flat
- 10 x 2 bed houses
- 21 x 3 bed houses
- 1 x 5 bed house
- •
- Spend (incl. Stamp Duty): £4.6m



- Number of properties brought in 2019/20: 183
- •
- 13 x 1 bed flats
- 22 bedsits
- 42 x 2 bed houses
- 104 x 3 bed houses
- 1 x 4 bed house
- 1 x 5 bed house
- •
- Spend (incl. Stamp Duty): £25.9m



- Number of properties brought in 2020/21: 109
- 1 x 1 bed flat
- 11 x 2 bed houses / bungalow / flat
- 88 x 3 bed houses
- 9 x 4 bed houses
- •
- Spend (incl. Stamp Duty): £20.5m



- Number of properties brought in 2021/22 (up to Wednesday 28<sup>th</sup> July 2021): \*194
- •
- 2 x 1 bed flats
- 3 x 2 bed house
- 15 x 3 bed houses
- \*174 units at Hospital Close
- •
- Spend (incl. Stamp Duty): £14.7m
- -----
- Total number of units acquired: 519
- •
- Total spend: £65.7m.



# Summary of acquisitions

type	18/19	19/20	20/21	21/22	In progress
Bed sits		22			
1 beds	1	13	1	2	9
2 beds	10	42	11	3	9
3 beds	21	104	88	15	52
4 beds		1	9		4
5 beds	1	1			
Hospital Close				174	
Totals (593)	33	183	109	194	74

# **Hospital Close**

#### The site



#### **Summary**

- Purchase completed on the 1<sup>st</sup> April 2021
- Comprised: 174 units
- Cost: £10.5m + stamp duty
- Price reflected the site was vacant and buildings were in need of reconfiguration and renovation

Leicester City Council

# **Current Challenges**

- Site is attracting regular fly tipping, ASB and vandalism
- 24 hour site security now in place and having a positive effect
- Taking a significant amount of time to secure and clear the site to enable the surveys to be undertaken



### **Proposed Programme**

- Emerging timescales:
- Aug 21 Planning Pre-application advice
- Dec 21 Planning application
- Dec 21 Tender exercise
- Apr 22 Contract appointments
- Jun 22 Start on site
- Dec 22 Sectional completions
- Autumn 23 Project Practical Completion



#### Manifesto commitment -1500

Delivery type	19/20	20/21	21/22	22/23	Total
New build by us	0	29	14	93	
Acquisitions - ours	183	109	757	100	
New build by others	144	8	53	19	
Acquisitions - others		19	0	0	
others	13	0	12	0	
totals	340	165	836	212	1553



#### How acquisitions are financed

- 40% from retained RTB receipts (30% prior to April 2021)
- 50% borrowing
- 10% from other receipts

